


S-Curve Showing Planned and Actual Work Progress The Construction of Mass Transit System Project in Bangkok (Red Line) (III) Contract 2 : Civil Works for Bang Sue - Rangsit Railway

(Based on Baseline Construction Schedule submitted via CC2/SRT/PM.470003 dated 22 Feb 2013 as well as Construction Schedule Rev.3.1A submitted via CC2/CSC/CS.031728 dated 13 Jun 2016)
+ Extended 100 days

Commencement Date 1,440 days
Contractual Period 1,440 days
Extension of Time SA No.4 Revised Period 1,905 days

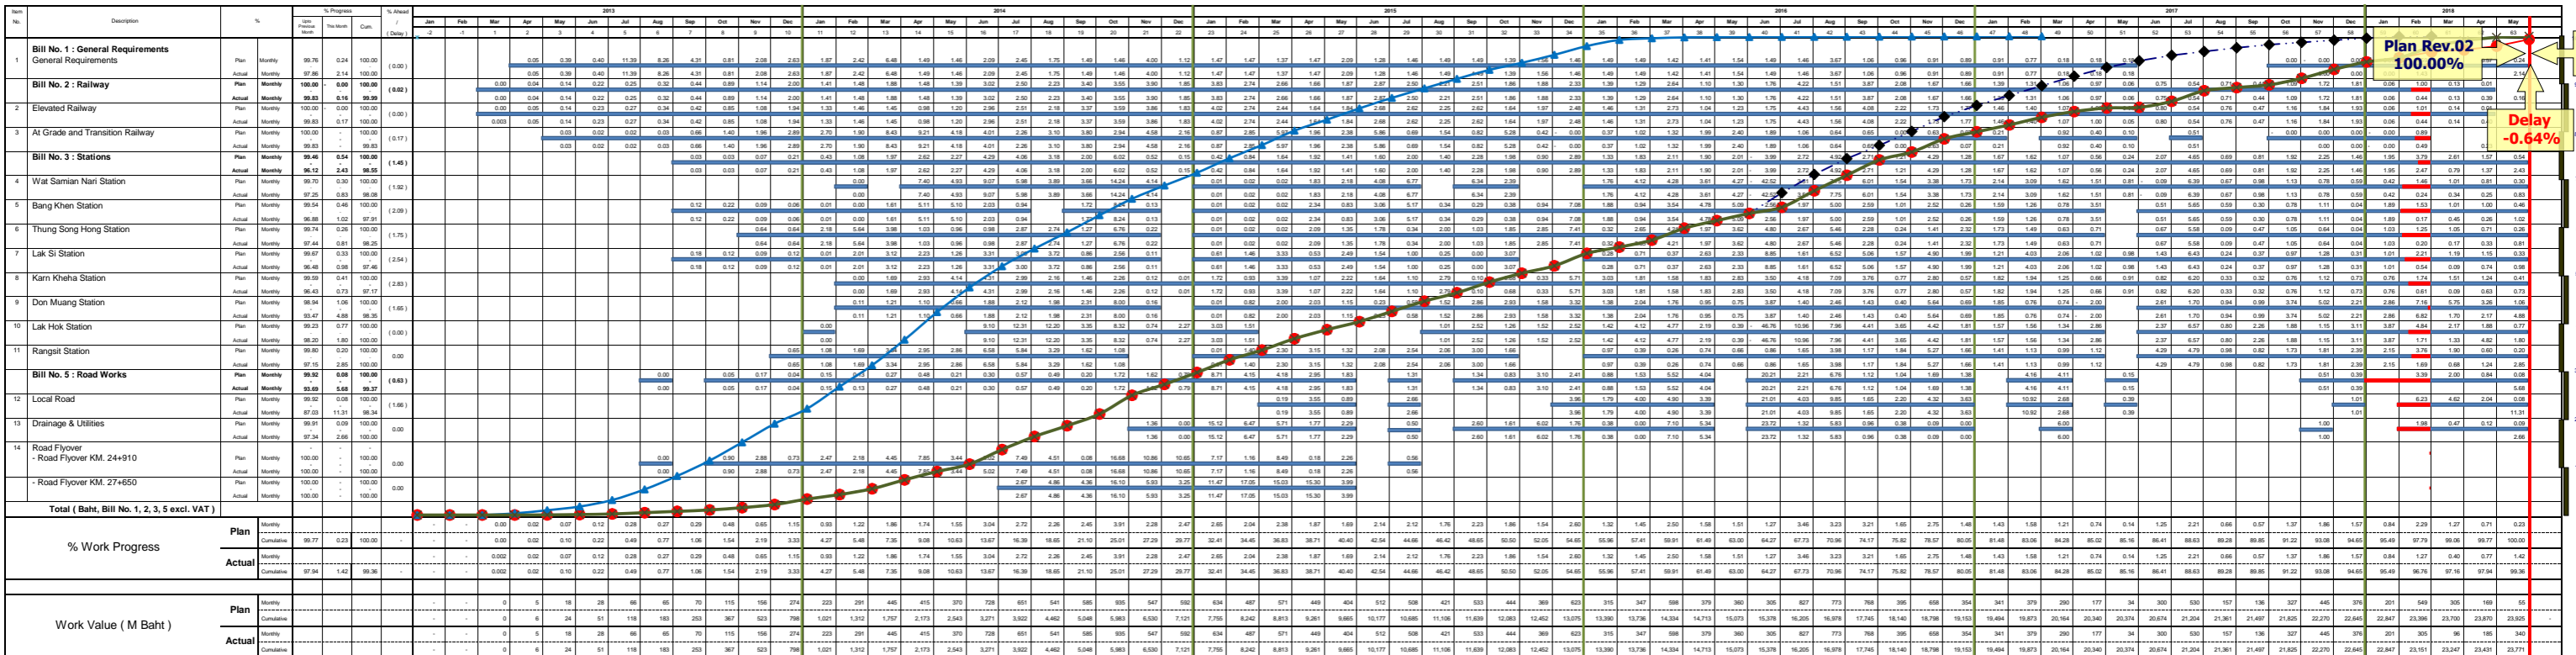

Plan Rev.02
100.00%

Act
99.3

Delay
-0.64%

Legend : ● Actual ▲ BaseLine ✕ Plan : 60M + Extended 100 days
