


**S-Curve (Rev.03) Showing Planned Percentage %
The Construction of Mass Transit System Project in Bangkok (Red Line) (II)
Contract 1 : Civil Works for Bang Sue Grand Station and Depots**

Redline: Revised Acceleration Detailed Works Programme (report date: 23 January 2017)

Commencement Date

4 Mar 13

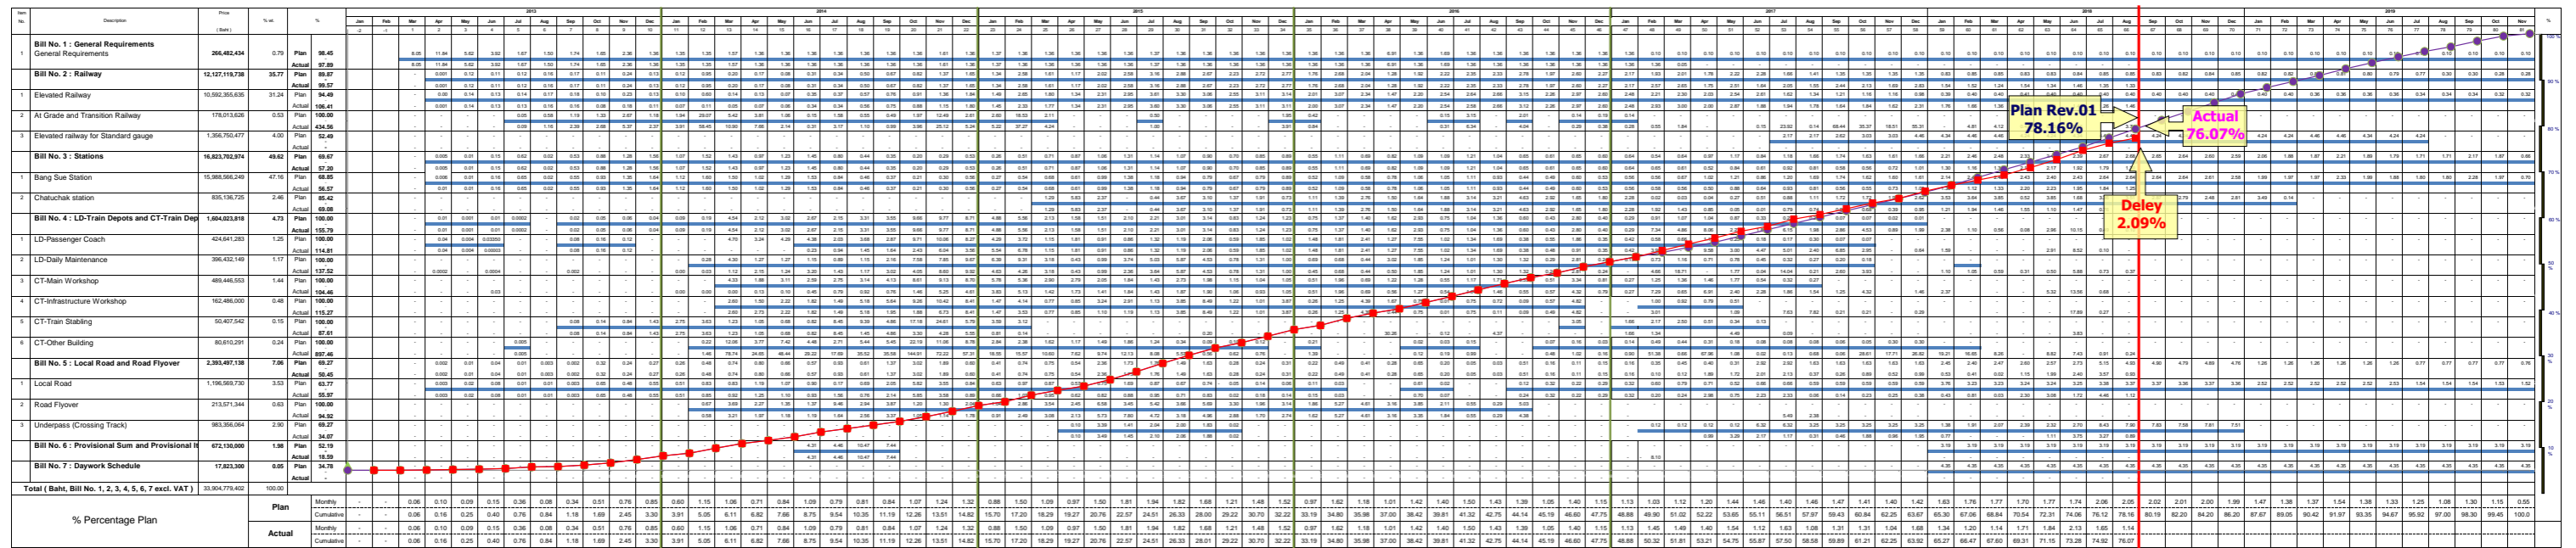

**Plan Rev.01
78.16%**

**Actual
76.07%**

**Delay
2.09%**
