


S-Curve Showing Planned and Actual Work Progress The Construction of Mass Transit System Project in Bangkok (Red Line) (III)

Contract 2 - Civil Works for Bang Sue - Rangsit Railway
+ Extended 100 days

Commencement Date 1,440 days
Extension of Time SA No.4 Revised Period 1,805 days

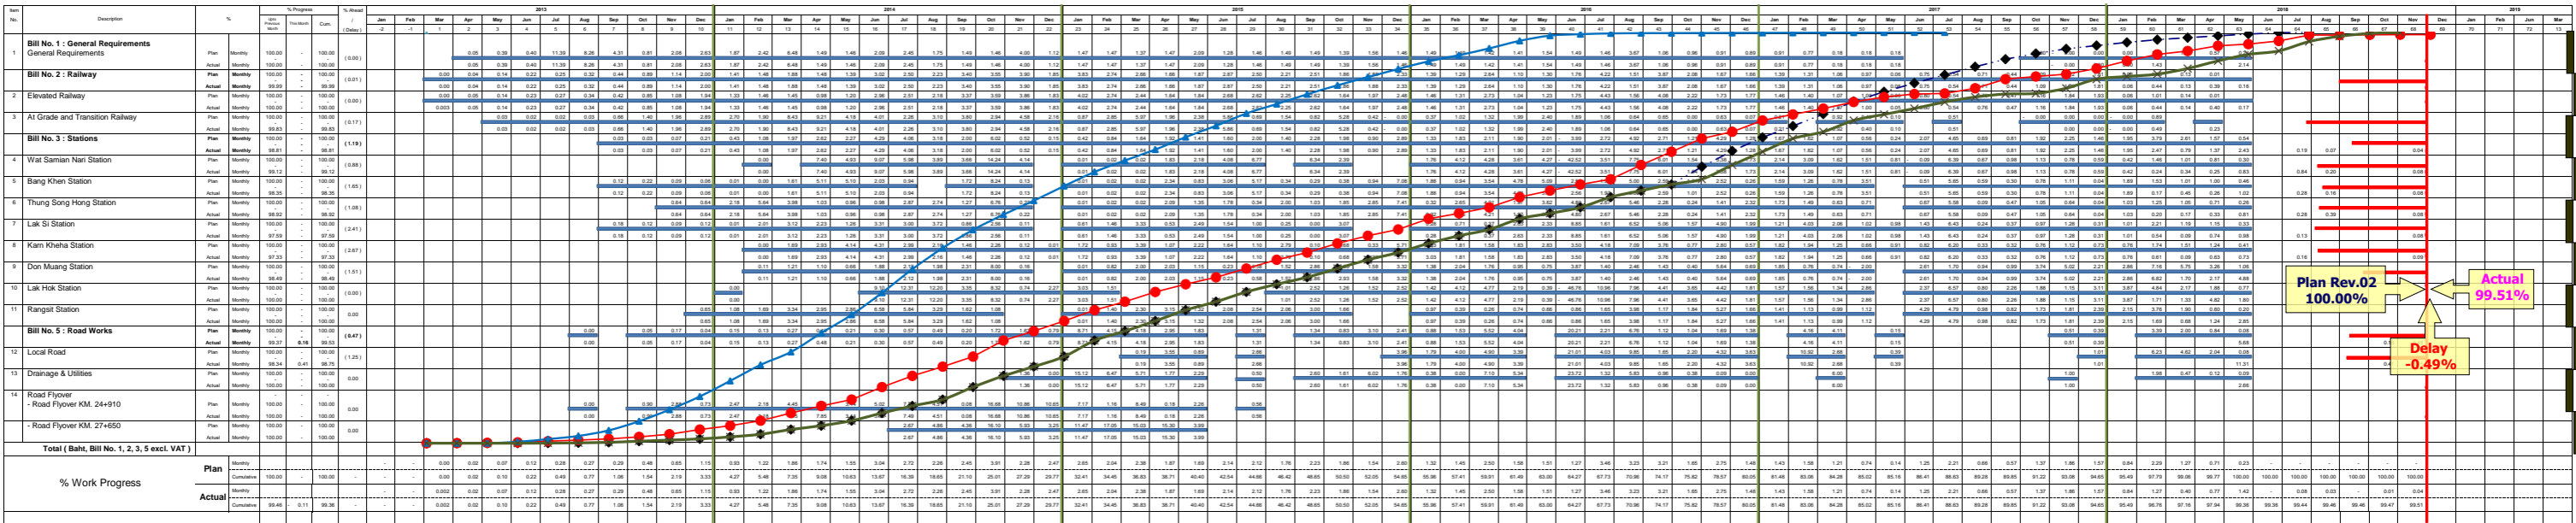

Legend : ● Actual ▲ BaseLine ✕ Plan : 60M + Extended 100 days

Plan Rev.02 100.00%
Actual 99.51%
Delay -0.49%
