S-Curve Showing Planned and Actual Work Progress

The Construction of Mass Transit System Project in Bangkok (Red Line) (III)

Contract 2 : Civil Works for Bang Sue - Rangsit Railway

(Based on Baseline Construction Schedule submitted via CC2/SRT/PM.470003 dated 22 Feb 2013 as well as Construction Schedule Rev.3.1A submitted via CC2/CSC/CS.031728 dated 13 Jun 2016)

+ Extended 100 days

Commencement Date — Contractual Period 1,440 days

Extention of Time SA No.4 — Revised Period 1,905 days

Item No.	Description		%	% Progress Upto Last Month	% Progress This Month	% Progress Cum.	% Ahead / (Delay)
1	**Bill No. 1 : General Requirements** General Requirements	Plan	Monthly	99.76	0.24	100.00	(0.00)
		Actual	Monthly	97.86	2.14	100.00	
	Bill No. 2 : Railway	**Plan**	**Monthly**	**100.00**	-	100.00	**(0.01)**
		Actual	**Monthly**	**99.83**	**0.16**	99.99	
2	Elevated Railway	Plan	Monthly	100.00	-	100.00	(0.00)
		Actual	Monthly	99.83	0.17	100.00	
3	At Grade and Transition Railway	Plan	Monthly	100.00	-	100.00	(0.17)
		Actual	Monthly	99.83	-	99.83	
	Bill No. 3 : Stations	**Plan**	**Monthly**	**99.46**	**0.54**	100.00	**(1.07)**
		Actual	**Monthly**	**96.12**	**2.81**	98.93	
4	Wat Samian Nari Station	Plan	Monthly	99.70	0.30	100.00	(0.24)
		Actual	Monthly	97.25	2.51	99.76	
5	Bang Khen Station	Plan	Monthly	99.54	0.46	100.00	(1.53)
		Actual	Monthly	96.88	1.58	98.47	
6	Thung Song Hong Station	Plan	Monthly	99.74	0.26	100.00	(1.34)
		Actual	Monthly	97.44	1.22	98.66	
7	Lak Si Station	Plan	Monthly	99.67	0.33	100.00	(2.25)
		Actual	Monthly	96.48	1.27	97.75	
8	Kam Kheha Station	Plan	Monthly	99.59	0.41	100.00	(2.67)
		Actual	Monthly	96.43	0.89	97.33	
9	Don Muang Station	Plan	Monthly	99.84	0.16	100.00	(1.51)
		Actual	Monthly	93.47	5.02	98.49	
10	Lak Hok Station	Plan	Monthly	99.23	0.77	100.00	(0.00)
		Actual	Monthly	98.20	1.80	100.00	
11	Rangsit Station	Plan	Monthly	99.80	0.20	100.00	0.00
		Actual	Monthly	97.15	2.85	100.00	
	Bill No. 5 : Road Works	**Plan**	**Monthly**	**99.02**	**0.08**	100.00	**(0.63)**
		Actual	**Monthly**	**93.69**	**5.68**	99.37	
12	Local Road	Plan	Monthly	99.92	0.08	100.00	(1.66)
		Actual	Monthly	87.03	11.31	98.34	
13	Drainage & Utilities	Plan	Monthly	99.91	0.09	100.00	0.00
		Actual	Monthly	97.24	2.66	100.00	
14	Road Flyover - Road Flyover KM. 24+910	Plan	Monthly	100.00	-	100.00	0.00
		Actual	Monthly	100.00	-	100.00	
	- Road Flyover KM. 27+650	Plan	Monthly	100.00	-	100.00	0.00
		Actual	Monthly	100.00	-	100.00	
	Total (Baht, Bill No. 1, 2, 3, 5 excl. VAT)						
	% Work Progress	**Plan**	Monthly				
			Cumulative	99.77	0.23	100.00	
		Actual	Monthly				
			Cumulative	97.94	1.42	99.36	

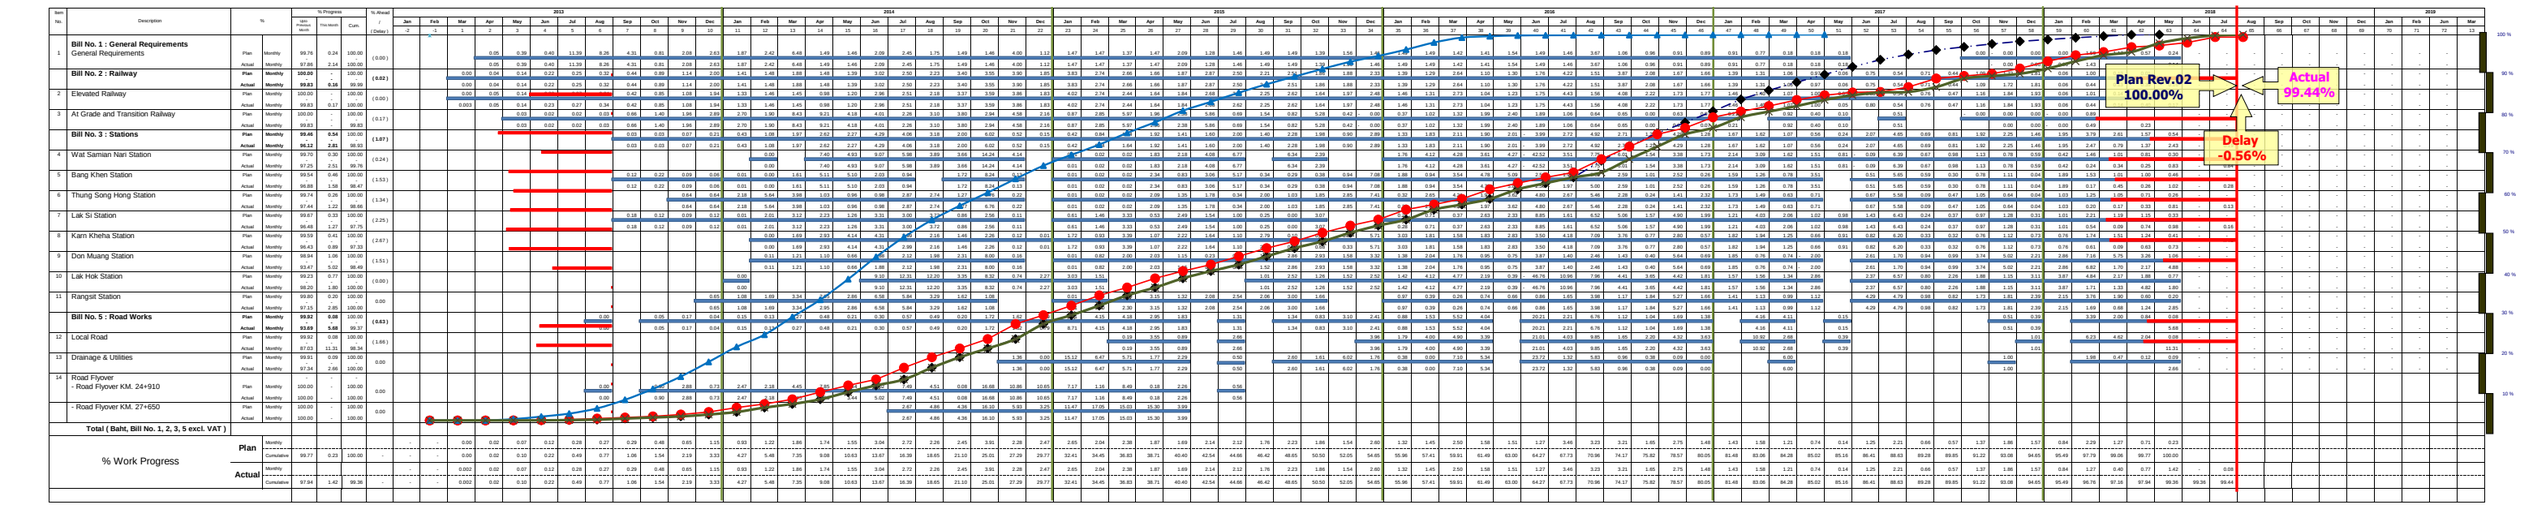

Legend : Actual — BaseLine — Plan : 60M + Extended 100 days
